

PHENIX Technical Support 2006

PHENIX Prep Schedule for Run 6


Don Lynch

1/11/2006

PHENIX Technical Support 2006

Prep Schedule for Run 6

- BBC N&S dried, tested re-installed, final tested [DONE]
- MuTr FEE and anode purge lines dried [DONE]
- MuTr HV & LV repairs and tests [DONE]
- Install Lampshades on MMS [DONE]
- Receive MPC South (Received 1/8/06)
- Prepare EC for move to IR (carpenters) [DONE]
- Re-install seismic restraints on WC [DONE]
- Prepare MPC South (install LED's, bench elec. tests) [DONE]
- Uninstall TOF West Installation platform [DONE]
- Install MPC South [DONE]
- Install HBD rack (lower only) [TODAY]
- Move MUID collar to IR [DONE]
- Install MPC cable tray [DONE]

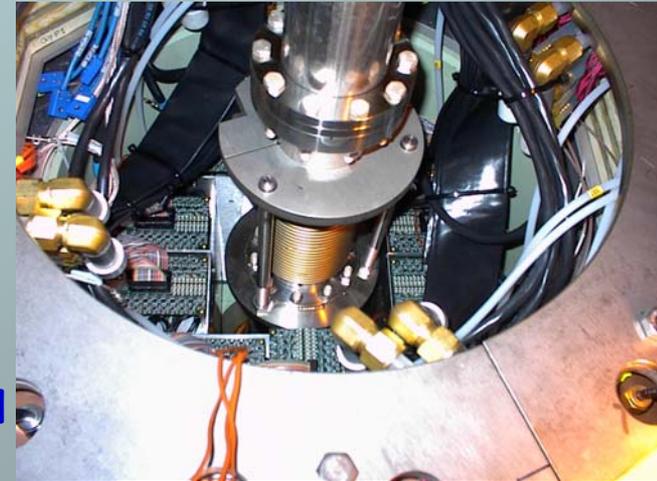

PHENIX Technical Support 2006

Prep Schedule for Run 6

Week of Jan. 17 - Jan. 20, 2006 (MLK Holiday 1/16/06)


- Complete CM area HBD plumbing
- Remove upper HBD I-beams, use fg unistrut for now [DONE]
- Continue MPC South installation
- EC roll in [Today] Carpenters to do platforms
- Start pink sheets

Week of Jan. 23 - Jan. 27, 2006

- CM area sweep for magnet test
- Magnet tests (blue sheets)
- Continue pink/blue sheets
- Connect EC Services
- Continue MPC South installation

Week of Jan. 30 - Feb. 3, 2006

- Install shield wall
- Complete MPC South installation
- Continue Pink sheet/ Blue sheets
- Move MMS North
- Install MUID collar
- Install Beam Loss Monitor
- DC repairs

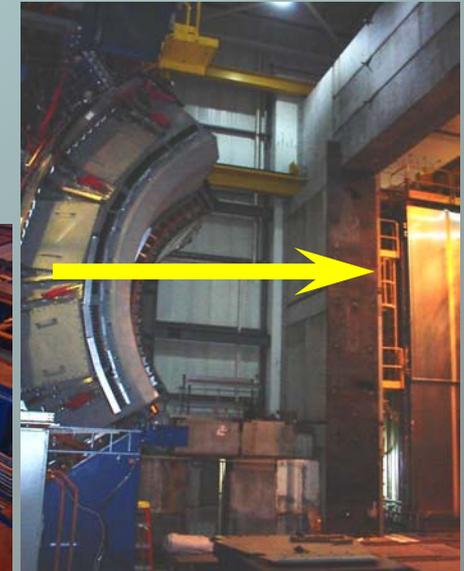

PHENIX Technical Support 2006

Prep Schedule for Run 6

Week of Feb. 6 - Feb. 10, 2006

- RXNP magnet tests
- Install plug door
- Start of PHENIX watch shifts
- Start flammable gas flow
- Blue ring ready for beam Feb. 6, limited IR access
- All up commissioning
- Start of Run Party

Week of Feb. 13- Feb. 17, 2006

- Yellow ring ready for beam
- All up commissioning

Week of Feb. 21 - Feb. 24, 2006 (Pres. Day Holiday 1/20/06)

- Start of run shifts

Week of Feb. 27 - Mar. 4

- Start physics runs
