PHENIX Technical Support 2006

PHENIX
C-A Coordination

05/08/06

Don Lynch

PHENIX

PHENIX Technical Support 2006

PHENIX Shutdown 2006

Task_Name	Duration	Start_Date	Finish_Date
PHENIX Shutdown '06	145 days	5/1/2006	11/17/2006
Pre Shutdown Tasks	60 days	5/1/2006	7/21/2006
End of Run 6	0 days	6/27/2006	6/27/2006
Shutdown Preparations	16 days	6/27/2006	7/18/2006
Detector Upgrades	47 days	7/19/2006	9/21/2006
Subsystem maint/repair tasks	47 days	7/19/2006	9/21/2006
Building and infrastructure tasks	113 days	5/1/2006	10/4/2006
E carriage roll in & setup	14 days	9/22/2006	10/11/2006
RHIC Cooldown Begins	0 days	10/16/2006	10/16/2006
Run Prep	25 days	10/16/2006	11/17/2006
Shutdown Concluded	0 days	11/17/2006	11/17/2006

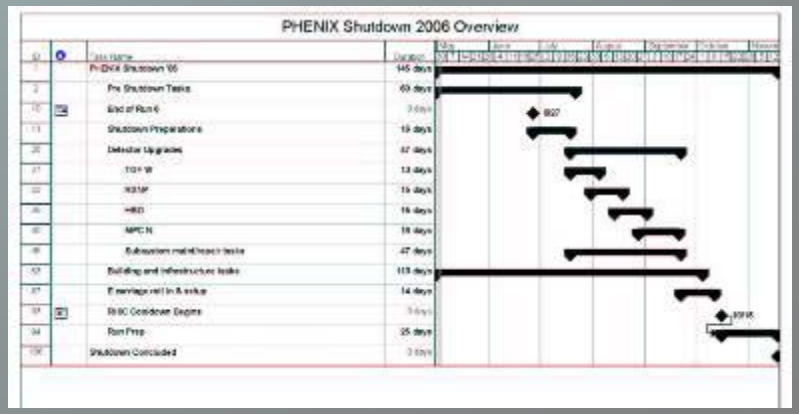

PHENIX

PHENIX Technical Support 2006

PHENIX Shutdown 2006

Pre Shutdown Tasks	60 days	5/1/2006	7/21/2006
Mechanical design For RXNP	4 wks	5/1/2006	5/26/2006
HBD cable mangement	4 wks	5/1/2006	5/26/2006
Receive TOF West detectors from VU	0 days	5/29/2006	5/29/2006
TOF West pre-installation tests (hi bay)	4 wks	5/29/2006	6/23/2006
Design mounting/install'n for MPC N	6 wks	5/29/2006	7/7/2006
Order/fabricate parts for RXNP/HBD/MPC N	12 wks	5/1/2006	7/21/2006
Design piping route for Bridge water	1 wk	7/10/2006	7/14/2006
End of Run 6	0 days	6/27/2006	6/27/2006



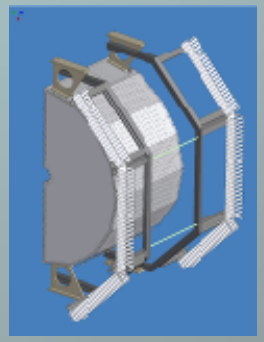

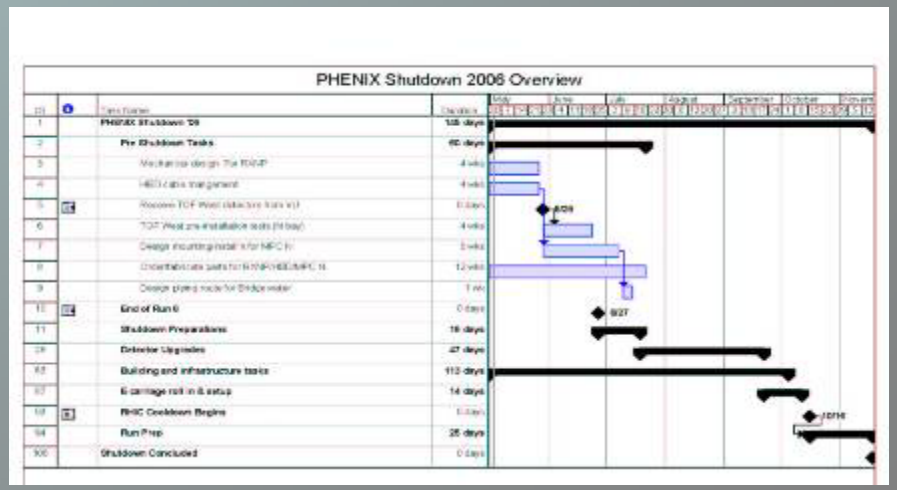

PHENIX

PHENIX Technical Support 2006

PHENIX Shutdown 2006

Shutdown Preparations	16 days	6/27/2006	7/18/2006
Purge gas from all detectors	2 days	6/27/2006	6/28/2006
End of Run party	0 days	6/29/2006	6/29/2006
DAQ tests	3 days	6/27/2006	6/29/2006
Open up & prep	1 day	6/30/2006	6/30/2006
Open rolling woor	1 day	6/30/2006	6/30/2006
Remove rolling wall and plug doors	1 wk	7/3/2006	7/7/2006
Take down EC access ladder & fold platforms	1 day	7/10/2006	7/10/2006
Prepare EC for move to AH	3 days	7/10/2006	7/12/2006
Remove beampipe collar	1 day	7/11/2006	7/11/2006
Move MMS full south and restrain	1 day	7/12/2006	7/12/2006
Retract and remove EC to AH	2 days	7/13/2006	7/14/2006
Install 12 ton cart on tracks	1 day	7/17/2006	7/17/2006
Move beampipe collar to AH	1 day	7/17/2006	7/17/2006
Install decking	1 day	7/18/2006	7/18/2006

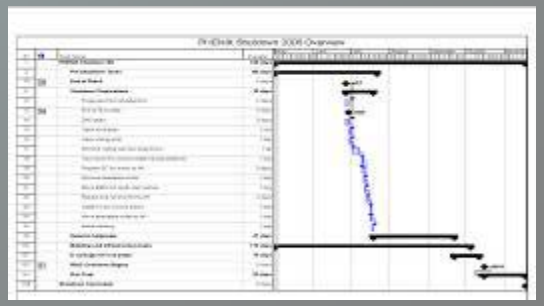

PHENIX

PHENIX Technical Support 2006

PHENIX Shutdown 2006

TOF W	13 days	7/19/2006	8/4/2006
Prepare installation Fixtures	2 days	7/19/2006	7/20/2006
Mockup test installation	1 day	7/21/2006	7/21/2006
TOF Mechanical installation	5 days	7/24/2006	7/28/2006
TOF Electrical Installation	5 days	7/31/2006	8/4/2006
RXNP	15 days	7/31/2006	8/18/2006
Prepare for installation	5 days	7/31/2006	8/4/2006
Mechanical installation	5 days	8/7/2006	8/11/2006
Electrical installation	5 days	8/14/2006	8/18/2006
HBD	15 days	8/14/2006	9/1/2006
Prepare for installation	5 days	8/14/2006	8/18/2006
Mechanical installation	5 days	8/21/2006	8/25/2006
Electrical installation	5 days	8/28/2006	9/1/2006
MPC N	18 days	8/28/2006	9/20/2006
Move CM south	2 days	8/28/2006	8/29/2006
Prepare for installation	5 days	8/30/2006	9/5/2006
Mechanical installation	5 days	9/6/2006	9/12/2006
Electrical installation	5 days	9/13/2006	9/19/2006
Move CM North	1 day	9/20/2006	9/20/2006

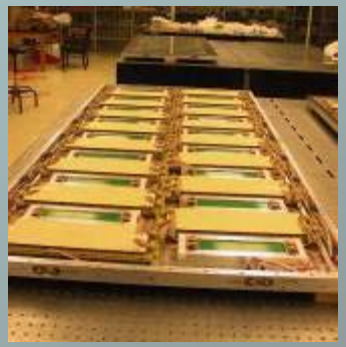

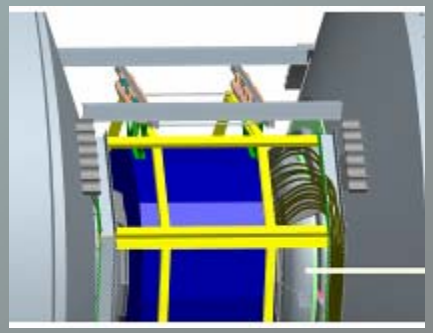

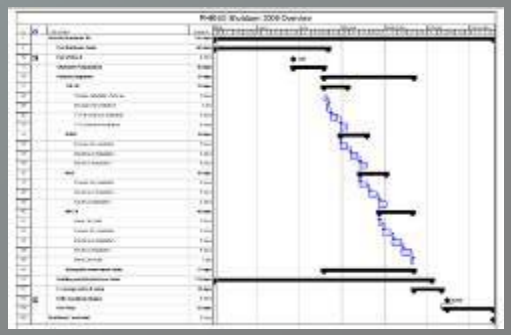

PHENIX

PHENIX Technical Support 2006

PHENIX Shutdown 2006

Subsystem maint/repair tasks	47 days	7/19/2006	9/21/2006
Prepare EC for subsystems work	1 wk	7/19/2006	7/25/2006
Magnet subsystems tasks (TBD)	1 day	7/19/2006	7/19/2006
Aerogel tasks (TBD)	1 day	7/20/2006	7/20/2006
BBC tasks (TBD)	1 day	7/21/2006	7/21/2006
DC tasks (TBD)	1 day	7/24/2006	7/24/2006
EmCal tasks (TBD)	1 day	7/26/2006	7/26/2006
FCAL tasks (TBD)	1 day	7/27/2006	7/27/2006
MPC S tasks (TBD)	2 wks	7/19/2006	8/1/2006
MuTr tasks (TBD)	1 day	8/2/2006	8/2/2006
MuID tasks (TBD)	1 day	8/3/2006	8/3/2006
PC tasks (TBD)	1 day	8/4/2006	8/4/2006
RICH tasks (TBD)	1 day	8/7/2006	8/7/2006
TEC tasks (TBD)	1 day	8/8/2006	8/8/2006
TOF E tasks (TBD)	1 day	8/9/2006	8/9/2006
ZDC tasks (TBD)	1 day	8/10/2006	8/10/2006
Other Subsystem tasks tasks (TBD)	6 wks	8/11/2006	9/21/2006

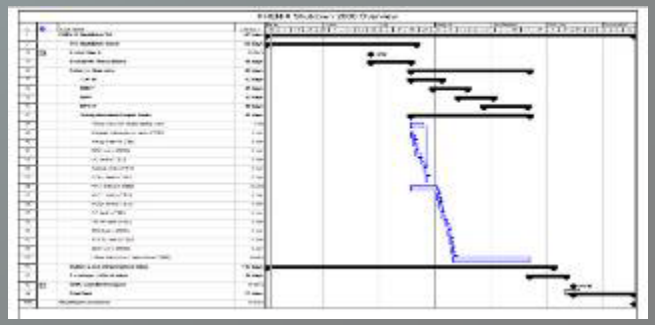

PHENIX

PHENIX Technical Support 2006

PHENIX Shutdown 2006

Building and infrastructure tasks	113 days	5/1/2006	10/4/2006
AH infrastructure tasks	1 day	5/1/2006	5/1/2006
TBD	1 day	5/1/2006	5/1/2006
IR infrastructure tasks	18 days	7/17/2006	8/9/2006
Repair water lines to Bridge	1 day	7/17/2006	7/17/2006
Replace emergency fan louvres	1 wk	7/19/2006	7/25/2006
Rewire/add IR Ceiling lights on emergency power	1 wk	7/26/2006	8/1/2006
Move WC away from Wall	1 day	8/2/2006	8/2/2006
Replace WC sliding platform hoisting cables	1 wk	8/3/2006	8/9/2006
Gas Pad	1 day	5/1/2006	5/1/2006
TBD	1 day	5/1/2006	5/1/2006
Gas Mixing House	1 day	5/1/2006	5/1/2006
Exhaust fan maintenance	1 day	5/1/2006	5/1/2006
TBD	1 day	5/1/2006	5/1/2006
Rack Room	1 day	5/1/2006	5/1/2006
TBD	1 day	5/1/2006	5/1/2006
Counting House	1 day	5/1/2006	5/1/2006
TBD	1 day	5/1/2006	5/1/2006
all other PHENIX infrastructure	113 days	5/1/2006	10/4/2006
Tech area & trailer mold remediation	1 day	5/1/2006	5/1/2006
New raw materials storage container	1 day	5/1/2006	5/1/2006
Repair roof leaks	1 day	5/1/2006	5/1/2006
Install bridge access platforms from EC & eyebrow	2 days	10/3/2006	10/4/2006
TBD	1 day	5/1/2006	5/1/2006

PHENIX

PHENIX Technical Support 2006

PHENIX Shutdown 2006

E carriage roll in & setup	14 days	9/22/2006	10/11/2006
Prepare EC for move to IR	1 wk	9/22/2006	9/28/2006
EC Roll in	2 days	9/29/2006	10/2/2006
Connect EC services	1 wk	10/3/2006	10/9/2006
Install EC Ladder	1 day	10/10/2006	10/10/2006
Install EC rear access & ext.	1 day	10/11/2006	10/11/2006
RHIC Cooldown Begins	0 days	10/16/2006	10/16/2006

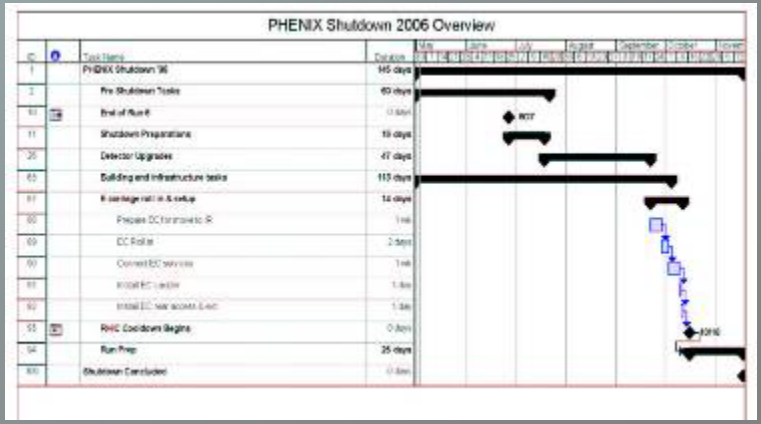

PHENIX

PHENIX Technical Support 2006

PHENIX Shutdown 2006

RHIC Cooldown Begins	0 days	10/16/2006	10/16/2006
Run Prep	25 days	10/16/2006	11/17/2006
Move MMS full North	1 day	10/16/2006	10/16/2006
Install beam pipe collar	1 day	10/17/2006	10/17/2006
Rebuild Rolling door	1 wk	10/18/2006	10/24/2006
Install Plug Door & steel platform	1 day	10/25/2006	10/25/2006
Close rolling door	1 day	10/26/2006	10/26/2006
Pink Sheeting & Blue Sheeting	2 wks	10/27/2006	11/9/2006
Start Flammable Gas Flow	1 day	11/10/2006	11/10/2006
All Up Commissioning	5 days	11/13/2006	11/17/2006
Beam in yellow ring	1 wk	11/13/2006	11/17/2006
Beam in blue ring	1 wk	11/13/2006	11/17/2006
RHIC beam conditioning	1 wk	11/13/2006	11/17/2006
Shutdown Concluded	0 days	11/17/2006	11/17/2006

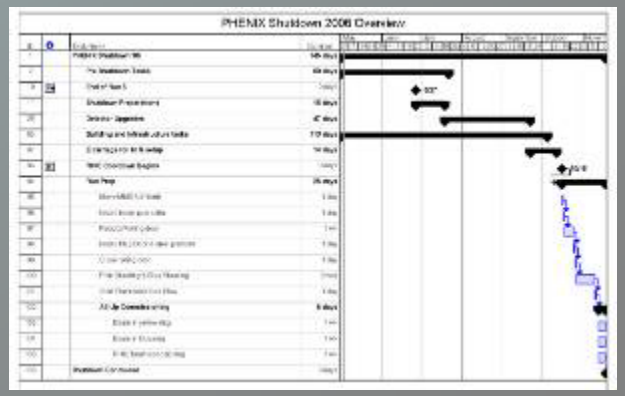

PHENIX

PHENIX Technical Support 2006

Shutdown 2006 key dates

- Run ends June 27
- End of Run Party June 29?
- Open Shield wall June 30
- Prep and move EC July 10
- Install TOF W (start) July 19
- Install RXNP (start) July 31
- Install HBD (start no later than) Aug 14 (possibly as early as Aug 1)
- Install MPC North (start no later than) Aug 28
- Start EC roll in Sep. 22
- Start RHIC Cooldown Oct. 15
- Start Physics data taking Nov. 17

PHENIX

PHENIX Technical Support 2006

HBD Prototype Run Position Mounting

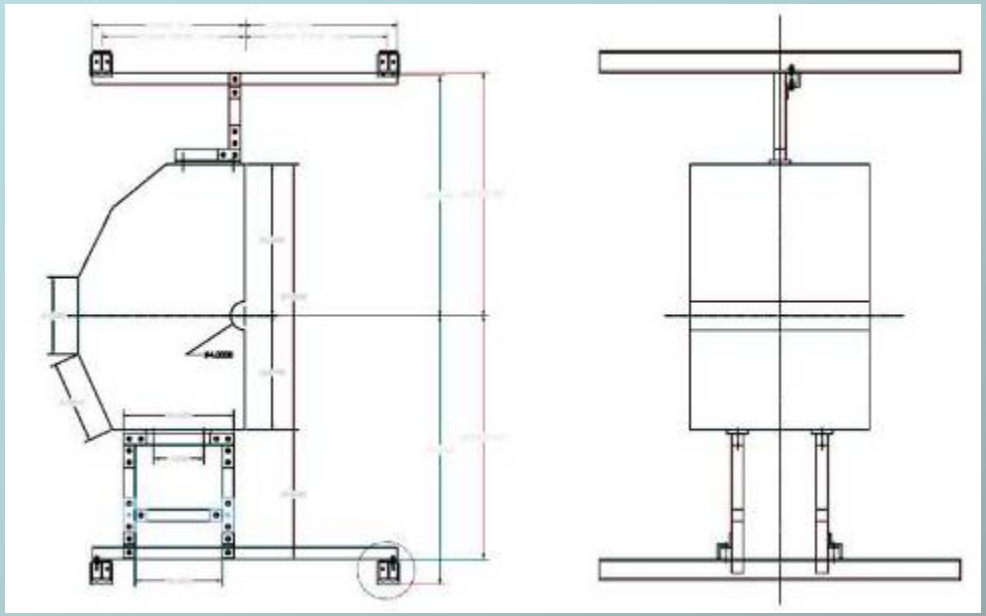

Prototype mounting supports

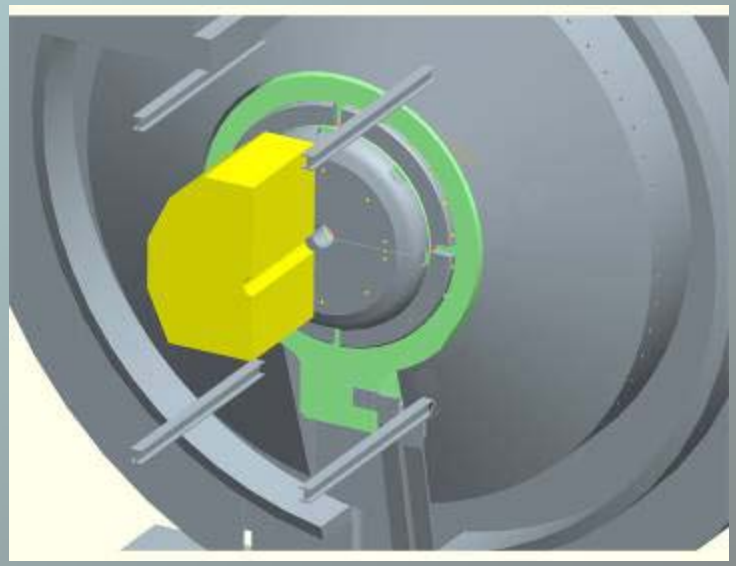

In run position
(mounting supports not shown)

When to take out He bag?

PHENIX

PHENIX Technical Support 2006

HBD & RXNP

Moved PMT's to 1300 mm max to avoid I-beams

3" PMT's

Attach arms to pole face for extra support

Still working on fiber routing/mounting/ protection

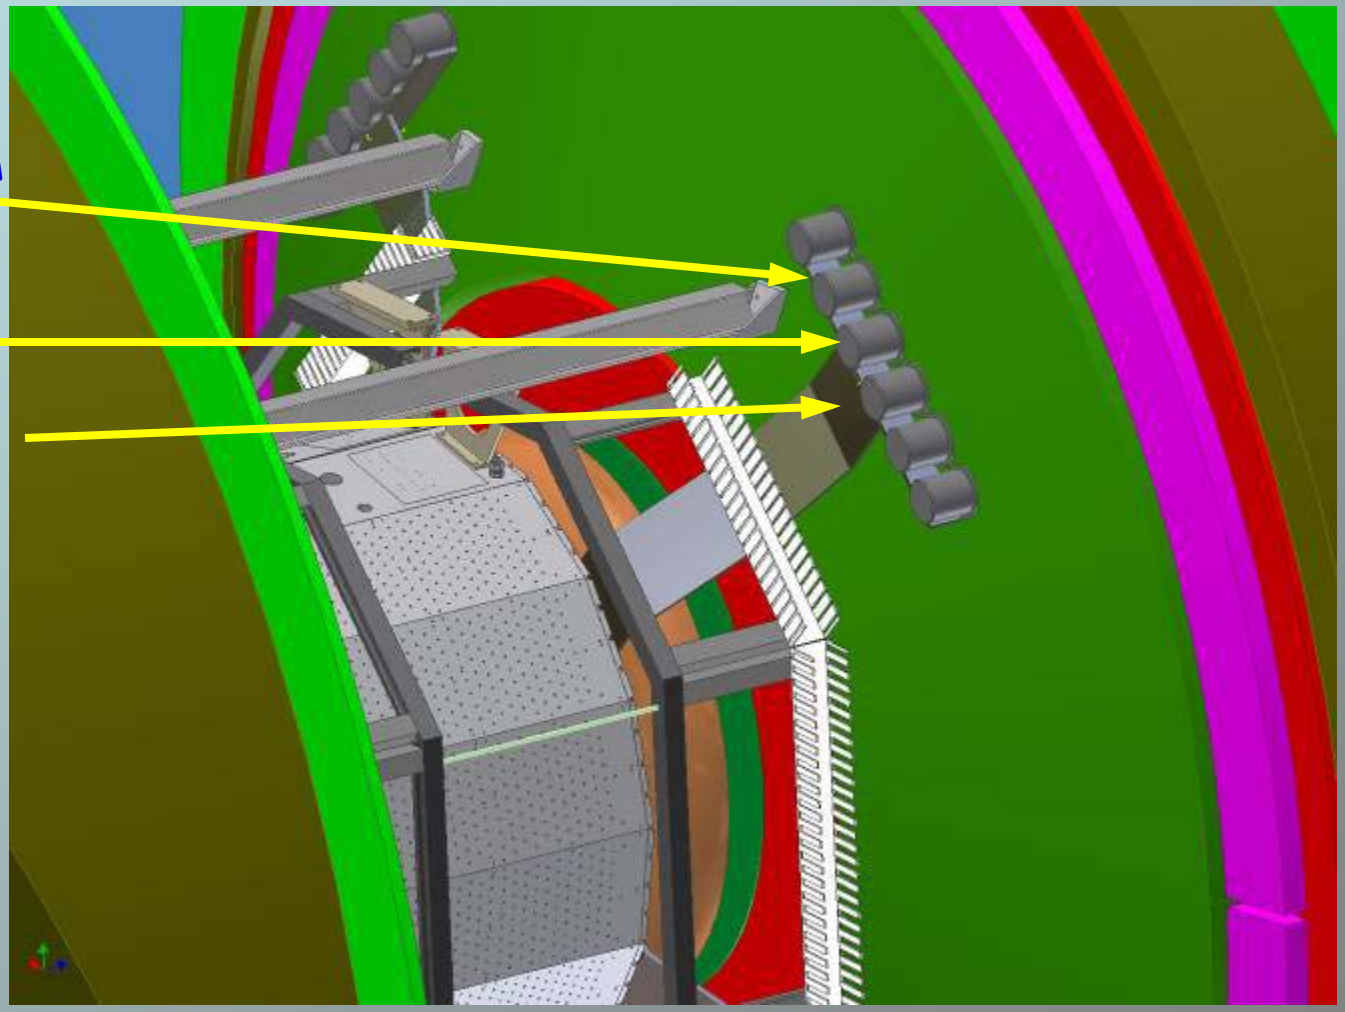

PHENIX

PHENIX Technical Support 2006

RXNP

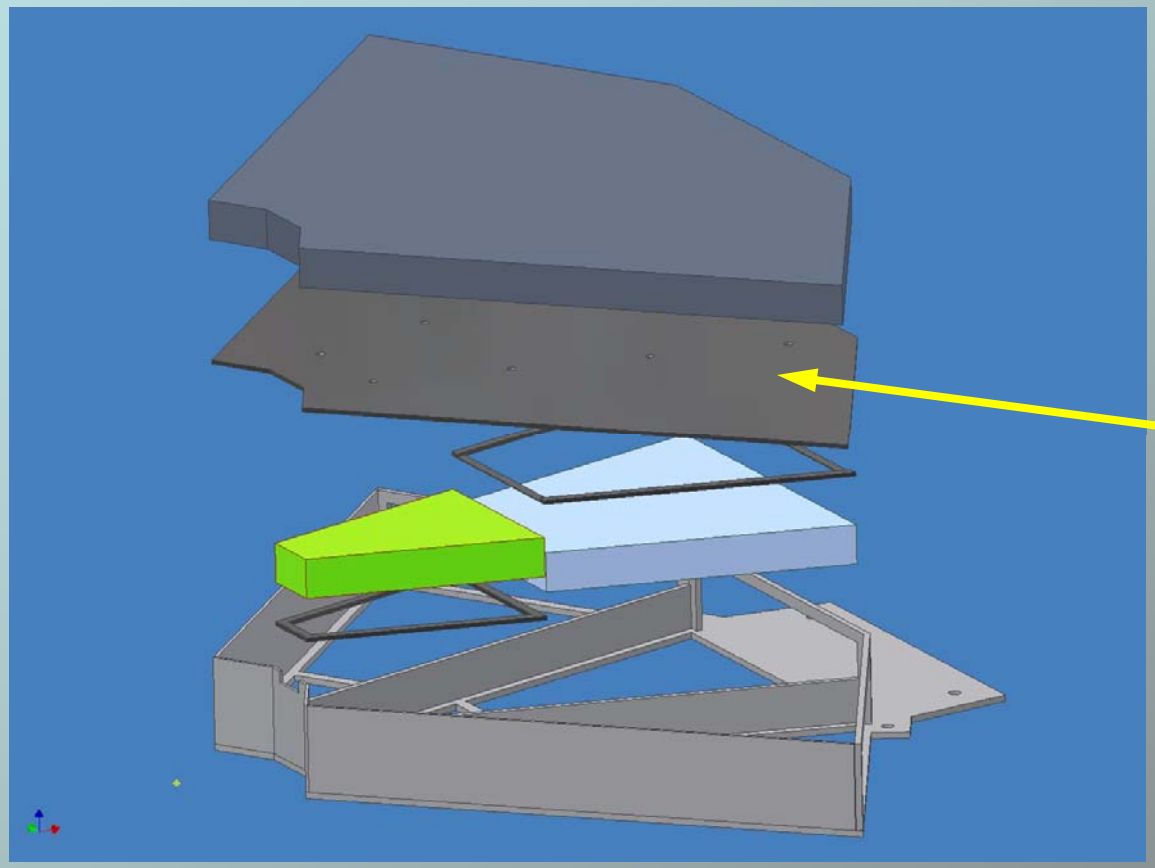

Revised design for RXNP

Spacer holds detector together without lead

PHENIX

PHENIX Technical Support 2006

RXNP Scintillator & Fiber Prototypes

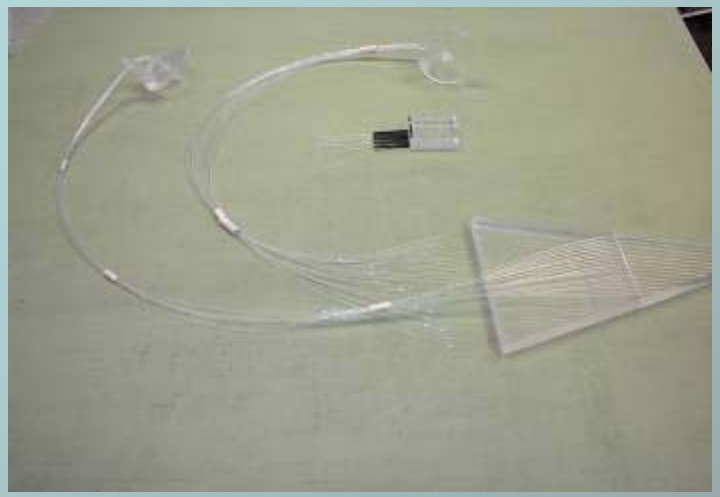

PHENIX
